



Main Fire Station

Project Location: SW corner of Foster Road and NW 1st Ave.



Project Description: The City’s Main Fire Station is over 40 years old and has outlived its useful life as well as exceeded the capacity and changes to the operations of the Fire Rescue Department. The new facility will include the City’s Emergency Operations Center, four drive-through bays, Fire Administrative Offices, Fire Inspection offices, training space, and living quarters.

ENGINEER/ARCHITECT


Currie Sowards Aguila Architects

CONTRACTOR

West Construction, Inc.

PROJECT PROGRESS: JUNE 2016

- Plans have been approved and permit is ready for pick up, awaiting payment.
- Remaining sub permit applications have been submitted to the city.
- Surveyors have layed out building corners and elevations.
- Batter boards have been installed for vibro compaction lay out.
- Rain tanks have been ordered and scheduled for delivery.
- Vibro compaction is scheduled to begin on 5-24-16, mobilizing equipment on 5-23-16.

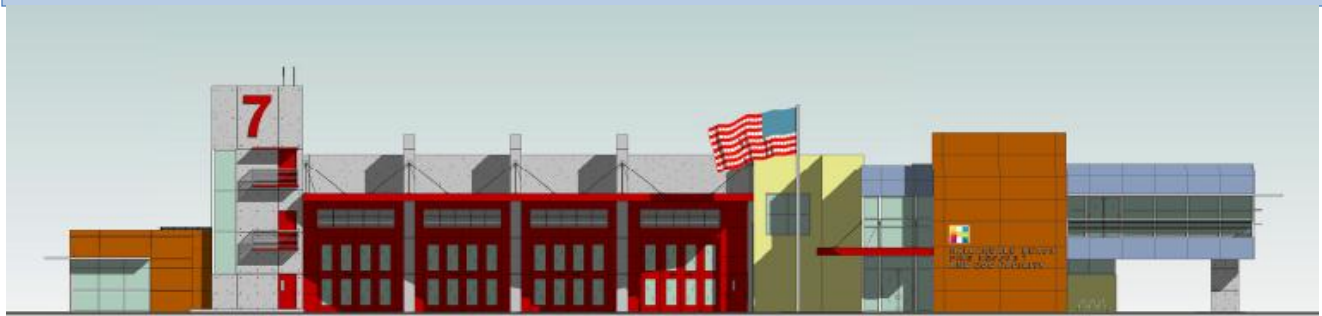

NORTH ELEVATION



TENTATIVE WORK SCHEDULE

100% Design	April 2014
Contractor Award	January 2016
Groundbreaking	March 18, 2016
Construction	14-16 months
Grand Opening	May 2017

CITY OF HALLANDALE BEACH – OFFICE OF CAPITAL IMPROVEMENT

CONTACT INFORMATION:

Director

Sarita Shamah

(954) 457-2995

sshamah@CoHB.org
